



TRANSPORTATION CLOSURE FORM

(Streets, Sidewalks, Bike Paths & Bike Parking)

Date Submitted: **3.29.2024**

Krannert Art Museum Roof Replacement

Street(s), Sidewalks, Bike Path or Parking to be Closed: **Northwest corner of Peabody Dr and 6th st.**

Intersecting Streets which are affected or define limits of closure: **None. Closure will affect sidewalk only**

Reason for Closure: **Vehicle pathway- Crane and material drop off to pick site. Sidewalk closure to ensure student traffic is not around trucks with heavy materials going through grass area. For safety and logistics concerns for heavy materials**

Project On-Site Contact Person:
U of I Project Manager (PM): **Nick Stanev**

Phone Number:
U of I PM Phone Number: **(217) 265-6789**

Date of Closure: **4.5.2024**

Expected Time of Closure: **Entirety of day**

Date of Re-opening: **5.5.2024**

Expected Time of Re-opening: **5.5.2024**

Work Order No. (if used):

CDB Contract No.:

Is Traffic re-routing necessary? **No**

If so, who should be involved? **Flagger, Site Superintendent**

Will Pedestrian/bicycle traffic be affected? **Yes, but open sidewalk is accessible**

If so, will the sidewalk be closed? **yes**

Will ADA audible/visual warnings and barriers be provided?

Will pedestrian traffic be routed safely? **Yes**

Choose an item.

Yes, signage

Are additional safety precautions needed? **No**

Please provide a diagram noting signage, re-routing, safety features, etc. with related explanations. **Diagram required.**

Yes No

☐☒

Is barricading required? If so, indicate the barricade locations on the diagram. You must contact the F&S Service Office to submit a barricade service request

☐☒

Will Facility & Services staff place the barricades?

If the barricades will be placed by others, give the name of person responsible and the telephone number: [Click or tap here to enter text.](#)

☐☒

Will police be necessary to direct the traffic? If so, name jurisdiction times, dates and location of each officer needed: [Click or tap here to enter text.](#)

☐☒

Will this street closure affect University of Illinois parking meters on the street or in the parking lots in this area? If so, you **MUST** contact the Parking Department at 333-3530 as there may be a fee assessed.

☐☒


Will MTD, DRES or other bus route re-locations be necessary? If so, coordinate with affected agency. Record name and date of discussion with agency representative: [Click or tap here to enter text.](#)

☒☐

Will deliveries be permitted? **If so, how will access be controlled?** [Click or tap here to enter text.](#)

Date approved: **4/9/24** ter a date. Approved By: **Stacey DeLorenzo**

Transportation Systems Manager (TSM): Stacey DeLorenzo · Phone: (217) 300-1750 · landscampustdm@illinois.edu

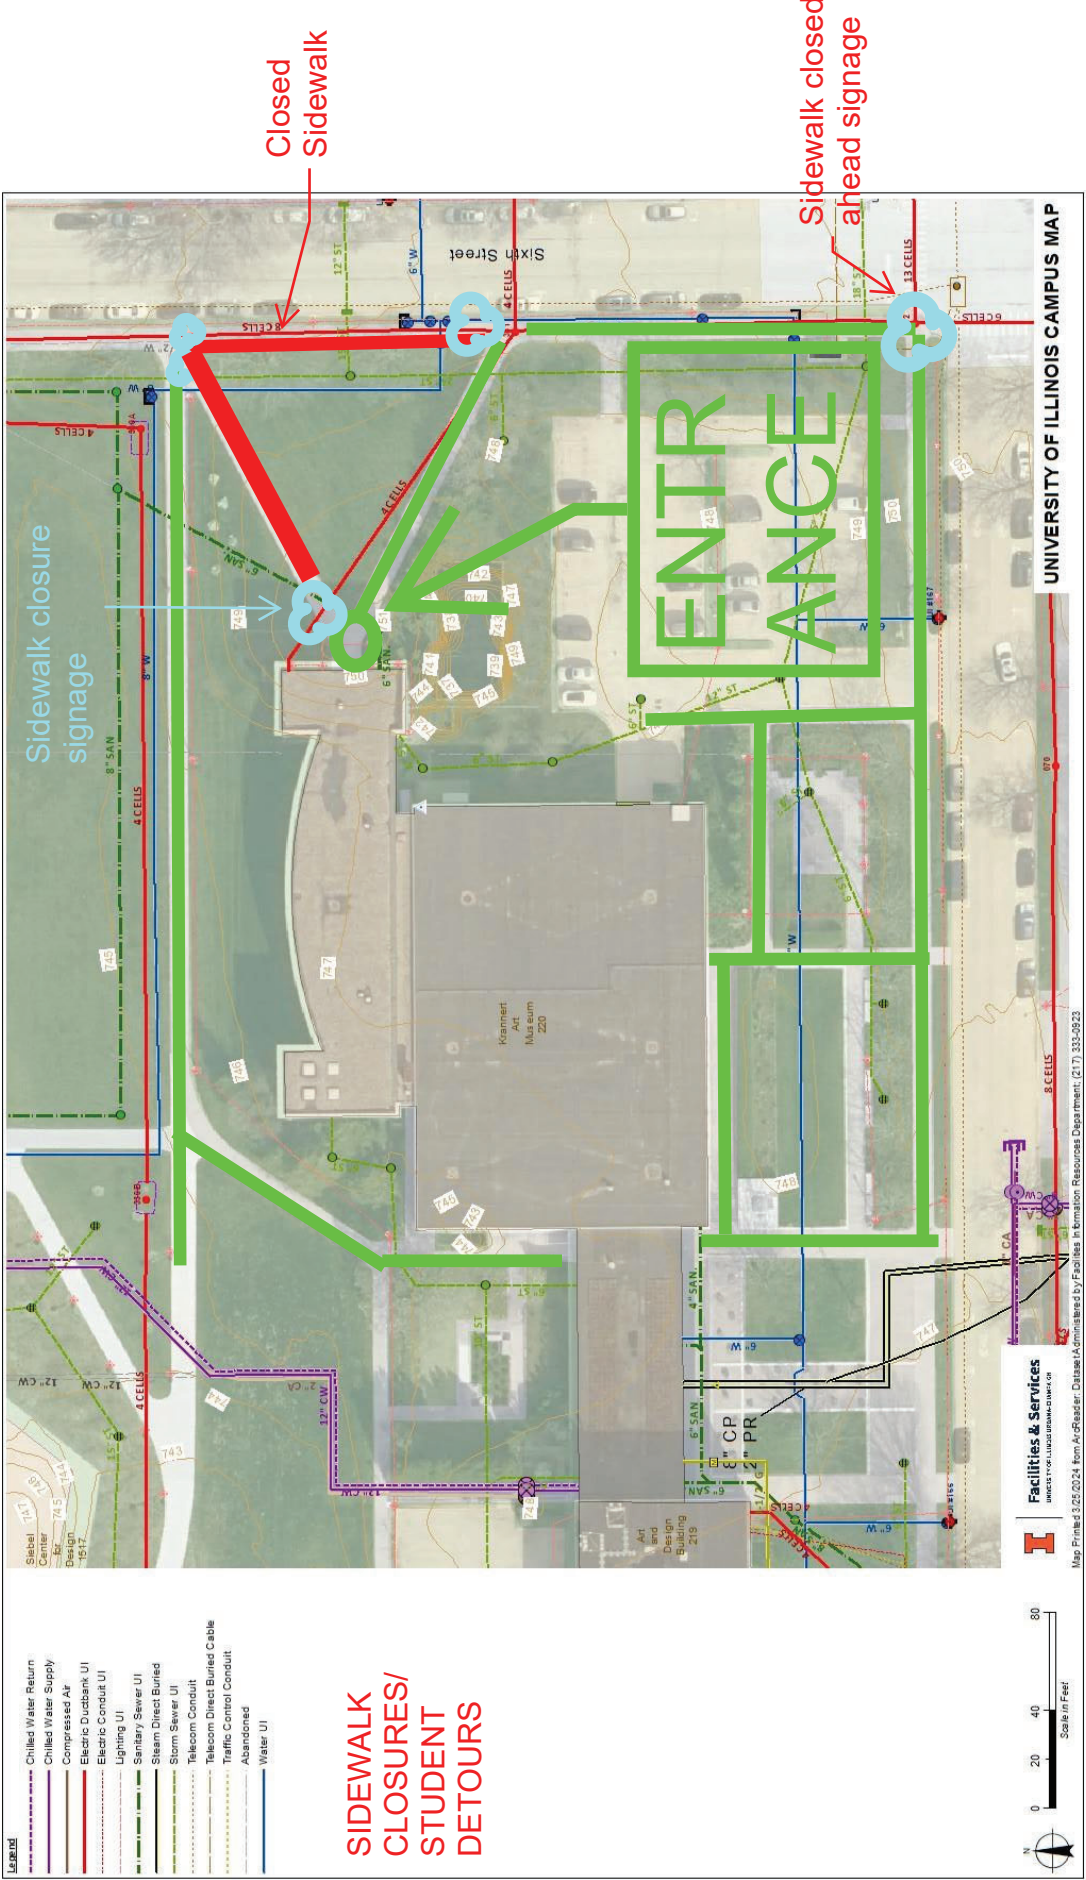

Side walk closure/ Student Detours

Red marked sidewalk will be closed for vehicle pathway

All green marked sidewalk will be available for student use.

No entrances will be temporarily closed with temporary canopies aiding student access to building.

Student foot traffic detour will have to utilize all open sidewalks and go around building if using main entrance on east side main door.

ENTRANCES WILL NOT BE CLOSED WITH OVERHEAD PROTECTION.


Gross Vehicle Weight Rating: 60,000 lbs.

This is a truck with crane attached. This is what will be used to hoist materials onto KAM. Not to be used for KCPA roofs.

Sidewalks are 8 inches thick in depth.

Ryan Welch, University Arborist advised sidewalks are sufficient enough for load.


Any damage to sidewalks will fall onto AGAE for repairs.

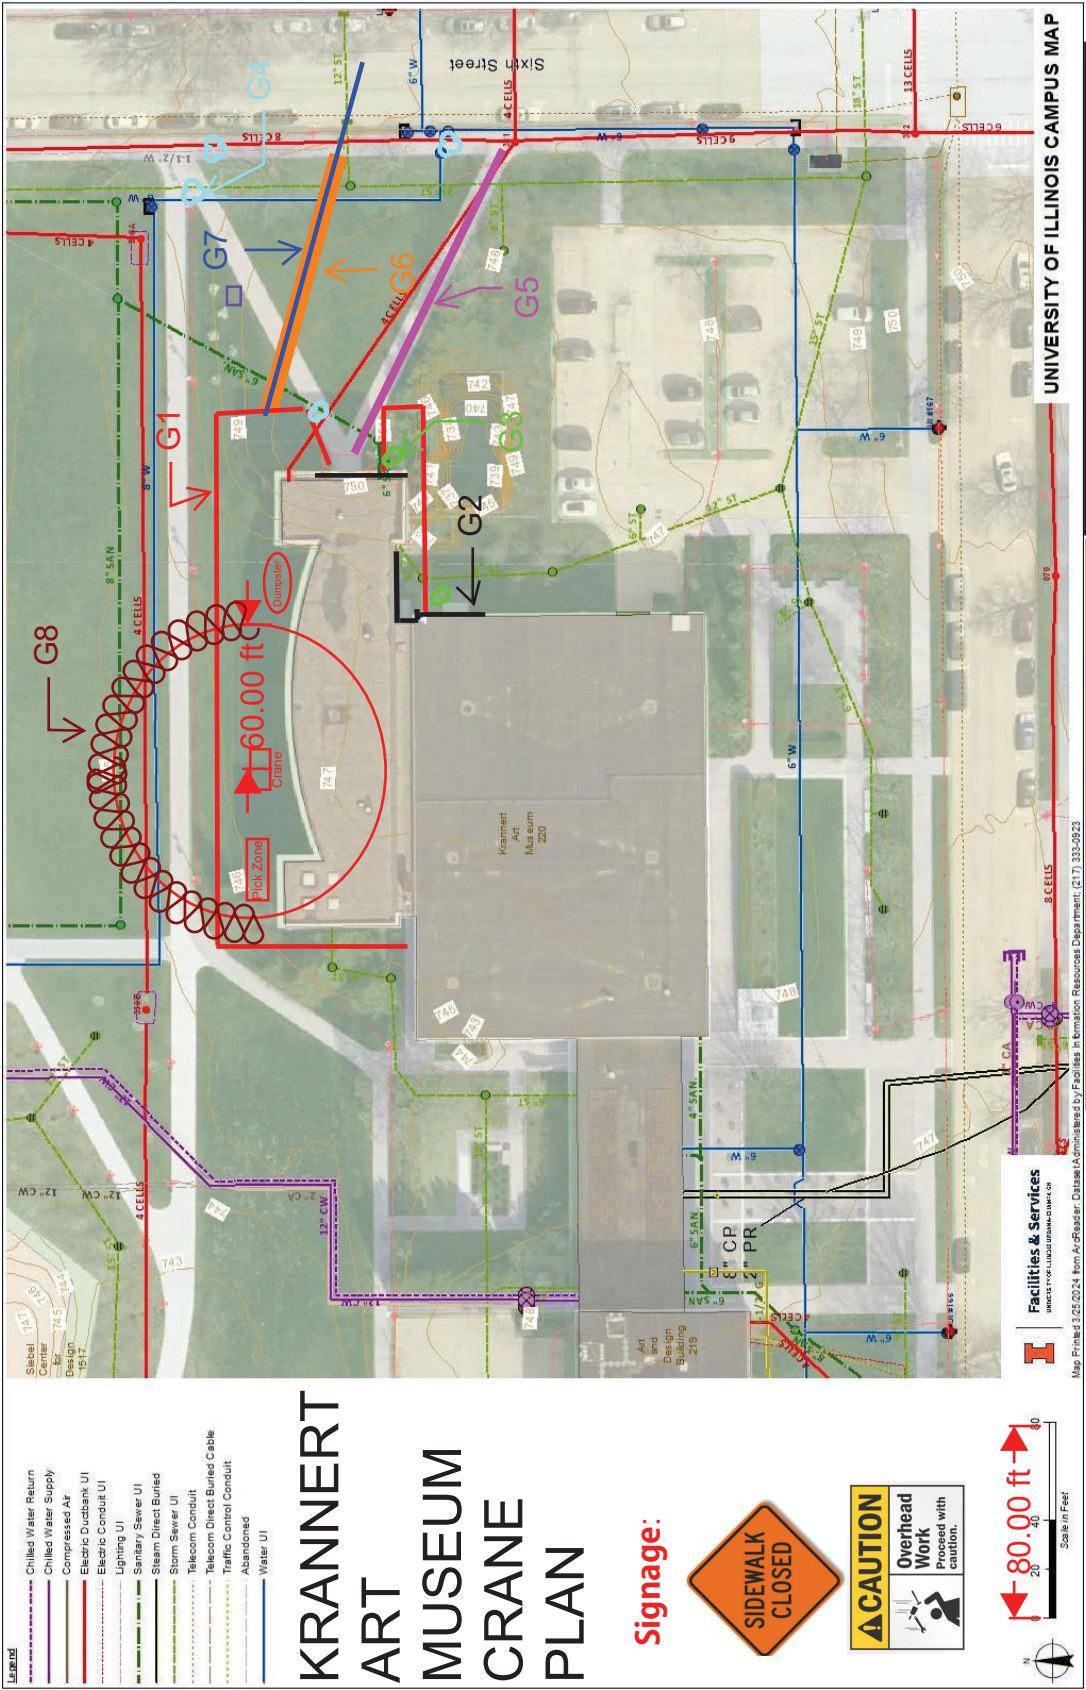

- Legend**
- Chilled Water Return
 - Chilled Water Supply
 - Compressed Air
 - Electric Ductbank UI
 - Electric Conduit UI
 - Lighting UI
 - Sanitary Sewer UI
 - Steam Direct Buried
 - Storm Sewer UI
 - Telecom Conduit
 - Telecom Direct Buried Cable
 - Traffic Control Conduit
 - Abandoned
 - Water UI

KRANNERT ART MUSEUM CRANE PLAN

Signage:



General Notes:

1. All entrances within pick area will be protected with temporary canopies.
2. All existing structures (ex: bike racks) will be protected
3. Crane will not swing any loads over street
4. Utilities are to be protected and no loads will be set up on top of steam tunnels.

KEY:

- G1- Fencing
- G2- Temp. Canopies
- G3-Overhead Work Signs
- G4- Sidewalk Closed Signs
- G5-Open Sidewalk for use
- G6- Landscape Protection
- G7- Vehicle Pathway
- G8- Portion of circumference will not be used for picks. Crane swing radius will not be utilized within area

Team Info: AGAE Contractors
 PM: Devin Dowling
 ddowling@agacontractors.com
 (312) 318-0858

Superintendent: Tim Fink
 tfink@agacontractors.com
 (773)771-2145

APM: Lisa Gonzalez
 Lgonzalez@agacontractors.com
 (772)805-0407
