






Gregory Dr Sixth St to Dorner Dr	11 days	Mon 6/3/24 8:00 AM	Mon 6/17/24 5:00 PM
Inlet Protection	2 days	Thu 5/30/24 8:00 AM	Thu 5/30/24 8:00 AM
Sawcuts	2 days	Thu 5/30/24 8:00 AM	Fri 5/31/24 8:00 AM
Curb Removal	1 day	Mon 6/3/24 8:00 AM	Tue 6/4/24 8:00 AM
Curb Replacement	2 days	Wed 6/5/24 12:00 PM	Thu 6/6/24 5:00 PM
HMA Surface Removal	3 days	Wed 6/5/24 8:00 AM	Fri 6/7/24 8:00 AM
Bituminous Tack Coat	1 day	Mon 6/10/24 12:00 PM	Mon 6/10/24 12:00 PM
HMA Binder Course	0.5 days	Tue 6/11/24 8:00 AM	Tue 6/11/24 8:00 AM
HMA Surface Course	1.5 days	Wed 6/12/24 12:00 PM	Thu 6/13/24 5:00 PM
Striping	1 day	Fri 6/14/24 8:00 AM	Fri 6/14/24 5:00 PM

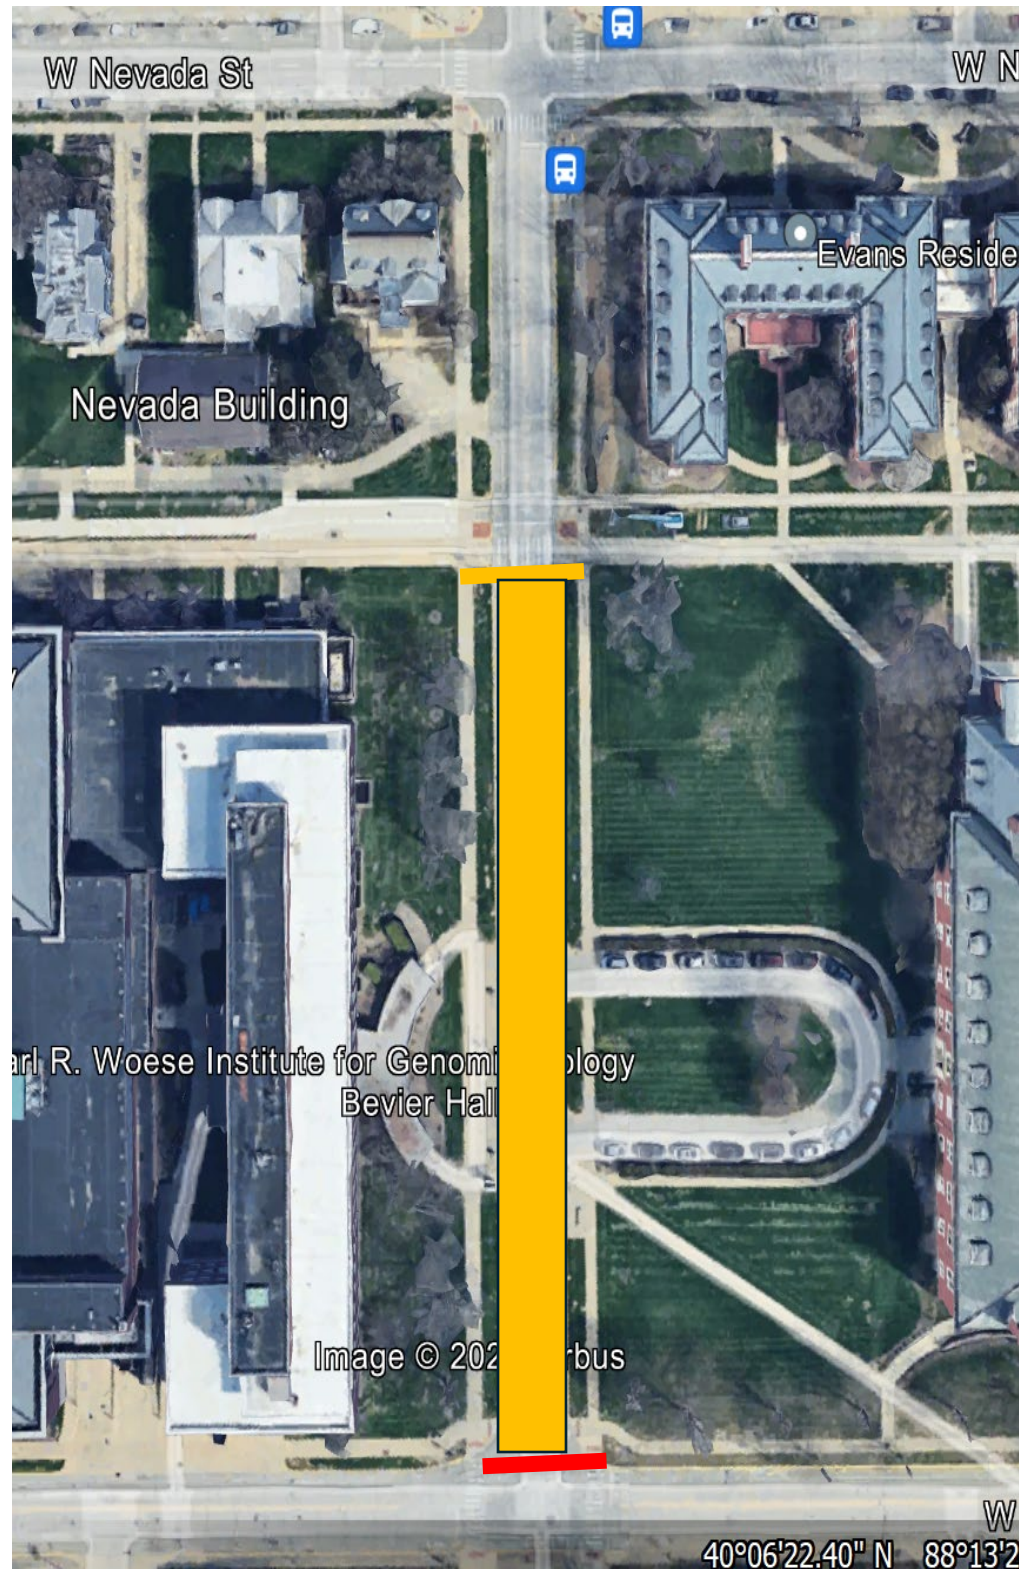

Goodwin Ave Gregory Dr to Nevada St	3 days	Tue 6/4/24 8:00 AM	Thu 6/6/24 5:00 PM
Inlet Protection	0.5 days	Tue 6/4/24 8:00 AM	Tue 6/4/24 12:00 PM
HMA Surface Removal	0.5 days	Wed 6/5/24 8:00 AM	Wed 6/5/24 12:00 PM
Bituminous Tack Coat	0.5 days	Fri 6/7/24 8:00 AM	Fri 6/7/24 12:00 PM
HMA Surface Course	0.5 days	Wed 6/12/24 8:00 AM	Wed 6/12/24 12:00 PM
Striping	1 day	Fri 6/14/24 8:00 AM	Fri 6/14/24 5:00 PM

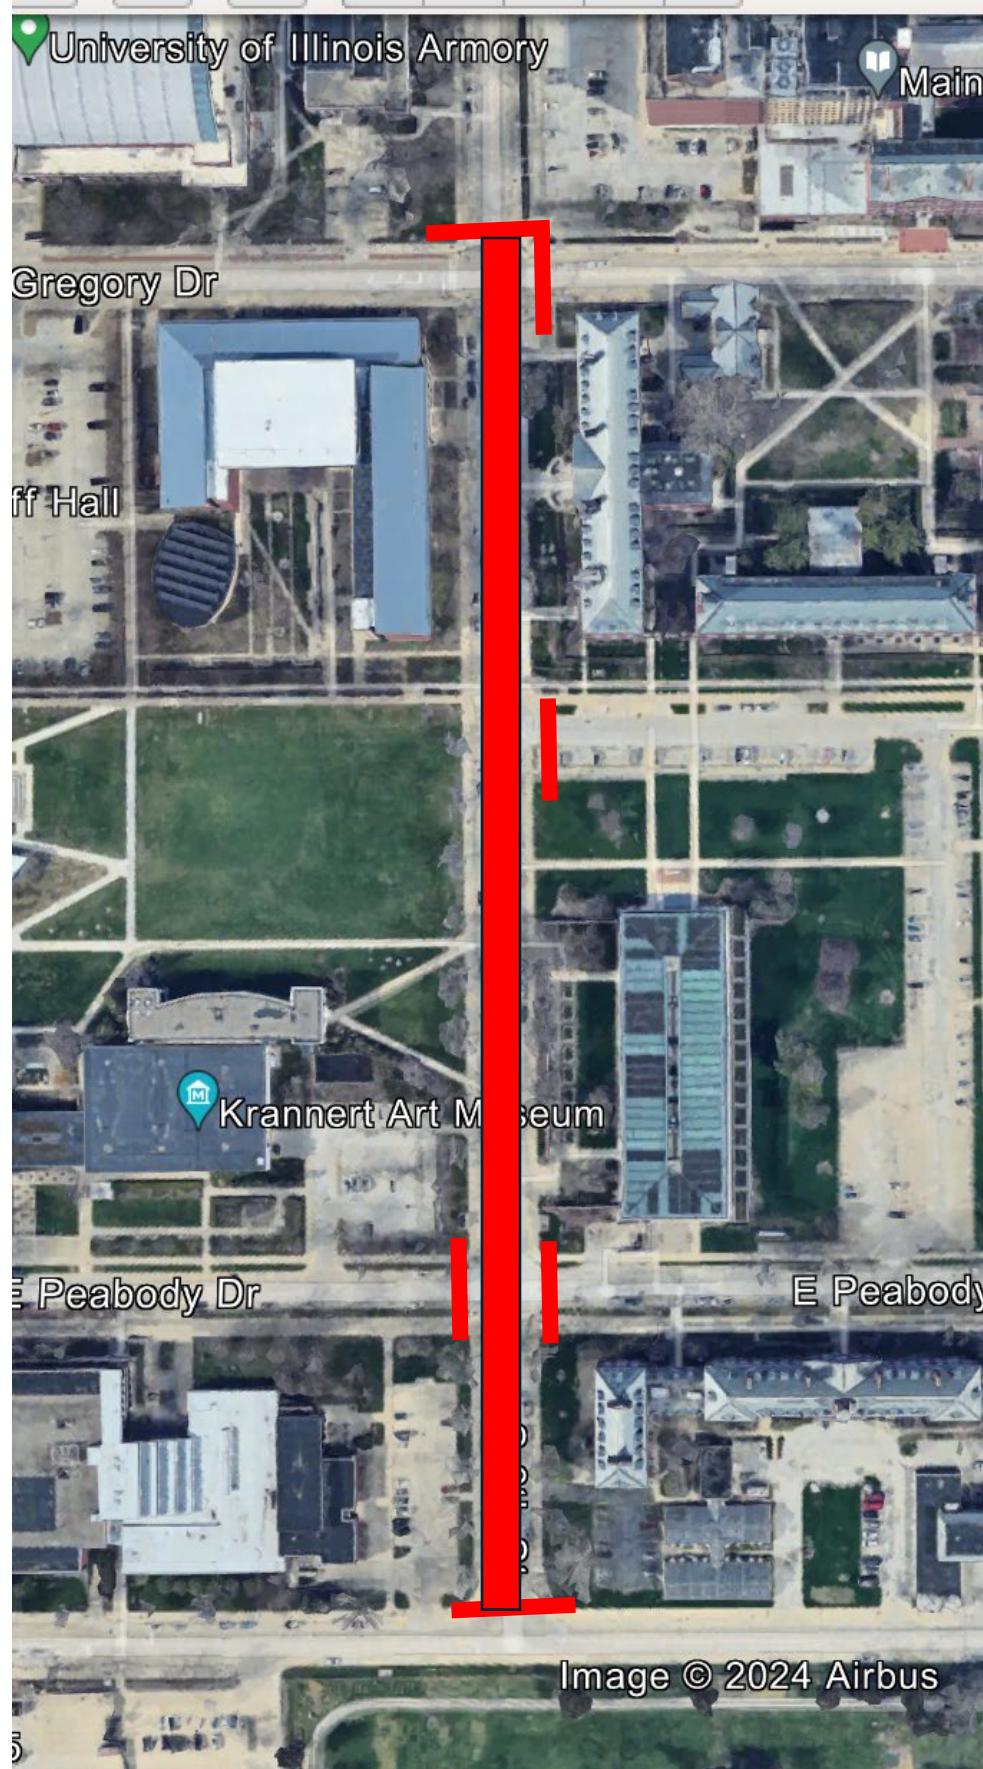

Sixth St - Gregory Dr to Pennsylvania Ave.	7 days	Fri 6/14/24 8:00 AM	Mon 6/24/24 5:00 PM
Inlet Protection	1 day	Fri 6/14/24 8:00 AM	Fri 6/14/24 5:00 PM
Curb and Gutter Removal	0.5 days	Mon 6/17/24 8:00 AM	Mon 6/17/24 5:00 PM
Curb and Gutter Replacement	0.5 days	Mon 6/17/24 8:00 AM	Mon 6/17/24 5:00 PM
HMA Surface Removal	1 day	Tue 6/18/24 8:00 AM	Tue 6/18/24 12:00 PM
Bituminous Tack Coat	1 day	Wed 6/19/24 8:00 AM	Wed 6/19/24 5:00 PM
HMA Binder Course	1 day	Thu 6/20/24 8:00 AM	Thu 6/20/24 5:00 PM
HMA Surface Course	1 day	Fri 6/21/24 8:00 AM	Fri 6/21/24 5:00 PM
Striping	1 day	Tue 6/25/24 8:00 AM	Tue 6/25/24 5:00 PM

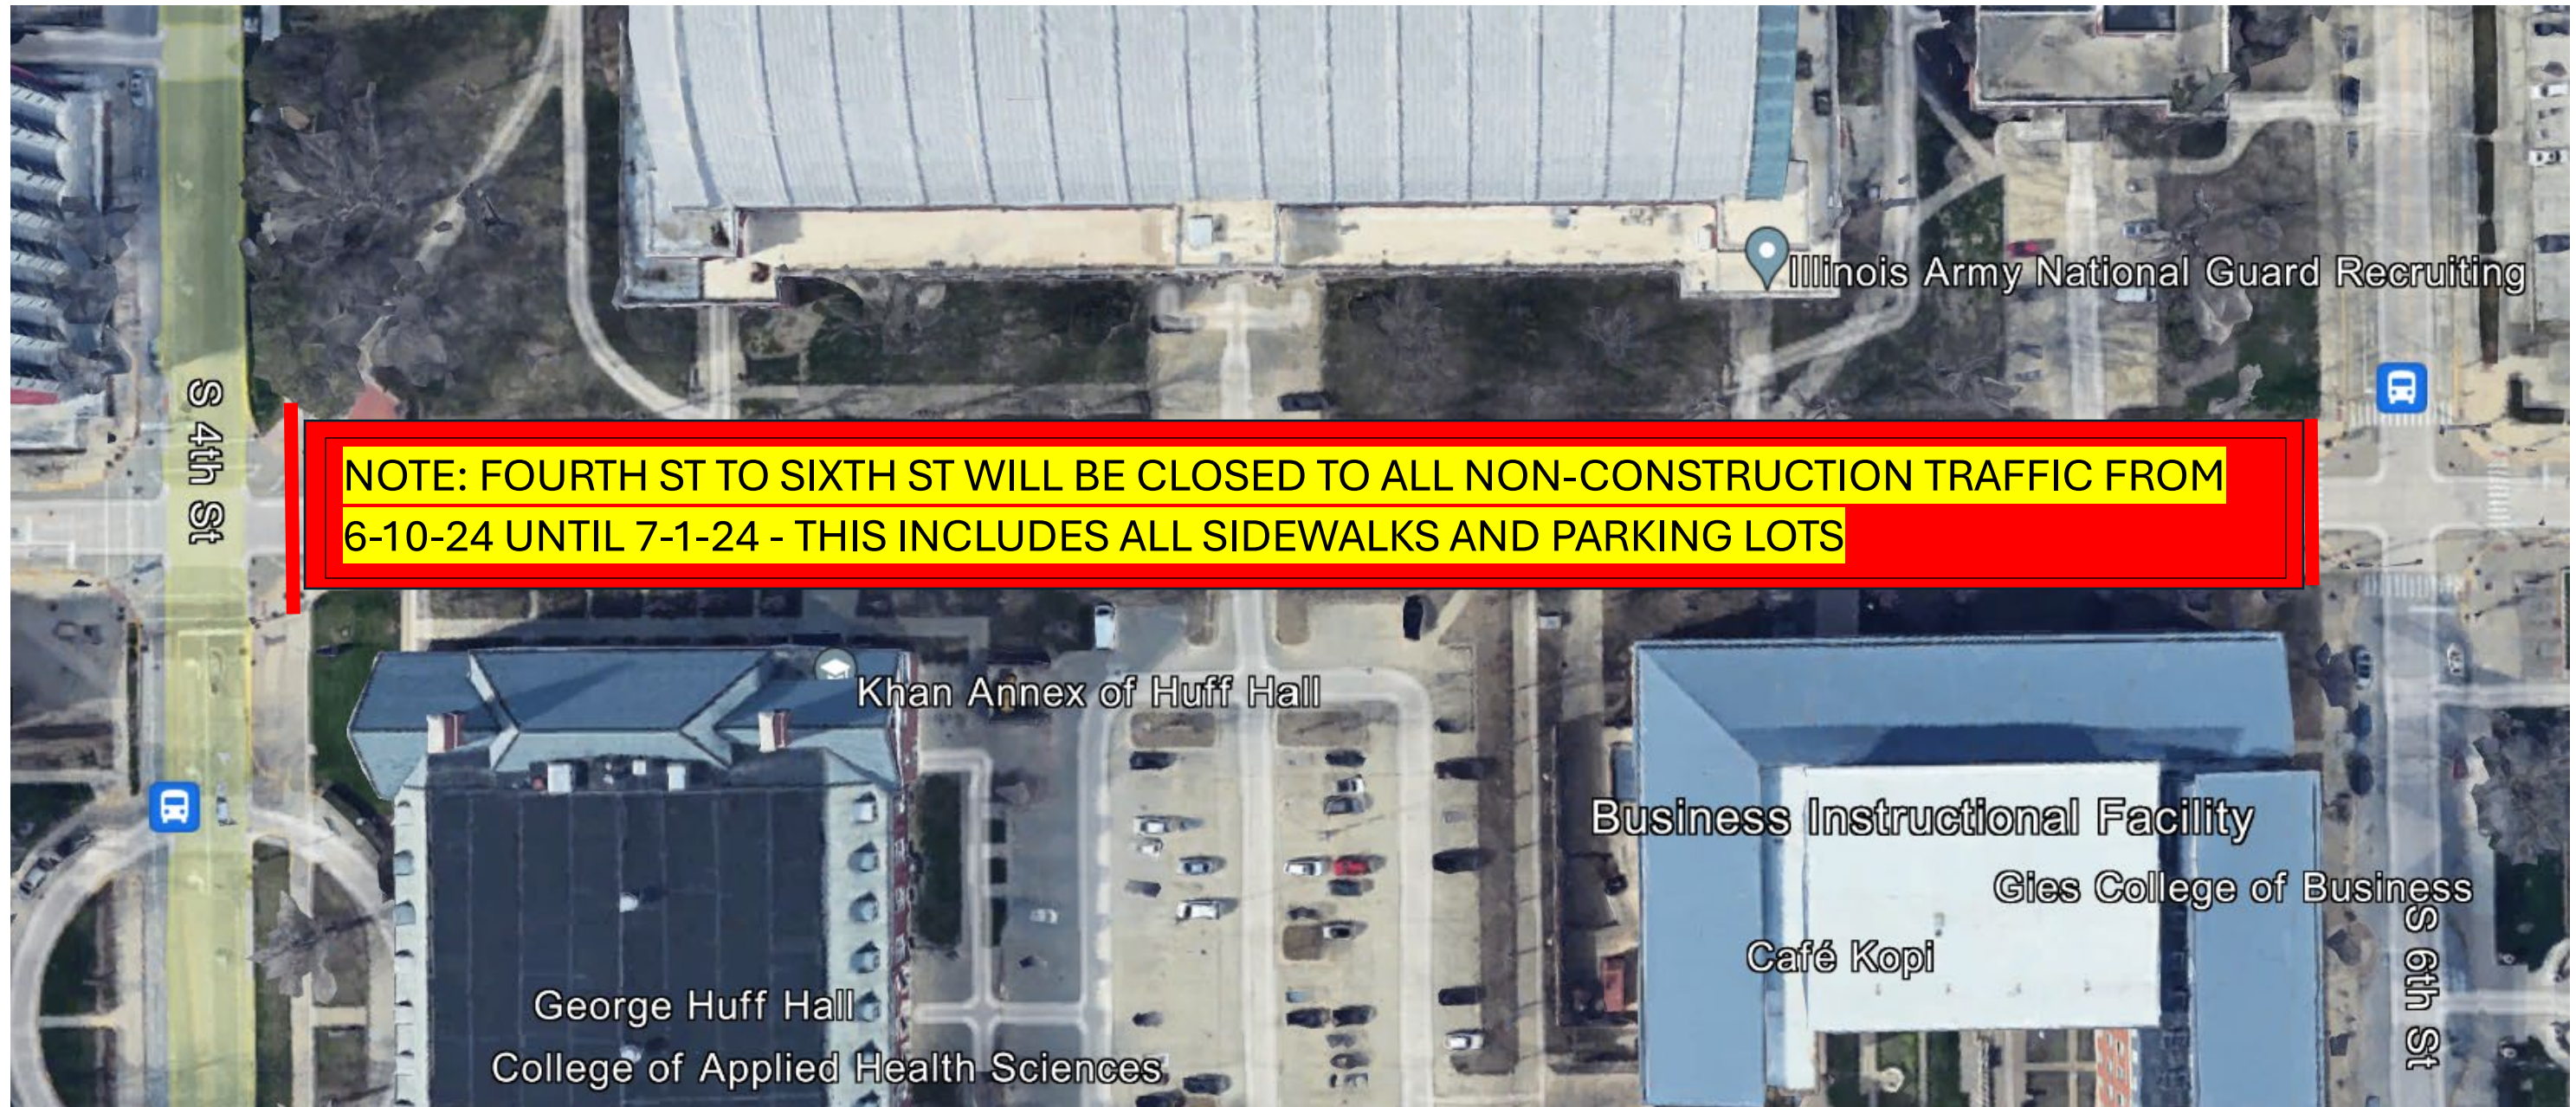

Gregory Dr Sixth to Fourth	8 days	Fri 6/14/24 8:00 AM	Tue 6/25/24 5:00 PM
Inlet Filters	1 day	Fri 6/14/24 8:00 AM	Fri 6/14/24 5:00 PM
HMA Surface Removal	1 day	Tue 6/18/24 8:00 AM	Tue 6/18/24 5:00 PM
Bituminous Tack Coat	1 day	Wed 6/19/24 8:00 AM	Wed 6/19/24 5:00 PM
HMA Surface Course	1 day	Fri 6/21/24 8:00 AM	Fri 6/21/24 5:00 PM
Striping	1 day	Tue 6/25/24 8:00 AM	Tue 6/25/24 5:00 PM



Gregory Dr 1st to 3rd	8 days	Fri 6/14/24 8:00 AM	Tue 6/25/24 5:00 PM
Inlet Filters	1 day	Fri 6/14/24 8:00 AM	Fri 6/14/24 5:00 PM
Curb Removal	0.5 days	Mon 6/17/24 8:00 AM	Mon 6/17/24 5:00 PM
Curb Replacement	0.5 days	Mon 6/17/24 8:00 AM	Mon 6/17/24 5:00 PM
HMA Surface Removal	1 day	Tue 6/18/24 8:00 AM	Tue 6/18/24 5:00 PM
Bituminous Tack Coat	1 day	Wed 6/19/24 8:00 AM	Wed 6/19/24 5:00 PM
HMA Surface Course	1 day	Fri 6/21/24 8:00 AM	Fri 6/21/24 5:00 PM
Striping	1 day	Tue 6/25/24 8:00 AM	Tue 6/25/24 5:00 PM



Gregory St Nevada to Oregon	3 days	Fri 6/21/24 8:00 AM	Tue 6/25/24 5:00 PM
Inlet Filters	1 day	Fri 6/21/24 8:00 AM	Fri 6/21/24 5:00 PM
HMA Surface Removal	0.25 days	Mon 6/24/24 8:00 AM	Mon 6/24/24 10:00 AM
HMA Binder Course	0.38 days	Mon 6/24/24 8:00 AM	Mon 6/24/24 11:02 AM
HMA Surface Course	0.38 days	Mon 6/24/24 8:00 AM	Mon 6/24/24 11:02 AM
Striping	1 day	Tue 6/25/24 8:00 AM	Tue 6/25/24 5:00 PM
